


SITE VISIT REPORT



ROSS-GOWER
a s s o c i a t e s
CONSULTING ENGINEERS

Project Name: Brooklyn Mews
Project No: 60163
Building Application No: B/2020/0584/
By: [REDACTED]
Date: 09/09/20
Weather: Sunny
Reason for visit: Check existing rafters on Unit 5.
Present: [REDACTED] (Kalmac), [REDACTED] Architect).
Distribution: [REDACTED] (BCO), [REDACTED] (Client)
Remarks:

- Existing gable wall at unit 6 has an unbonded chimney stack at second floor level. Refer to photographs 1 & 2. As repair works it is proposed to fill the gaps with mortar and install heavy duty straps as per the sketch below.

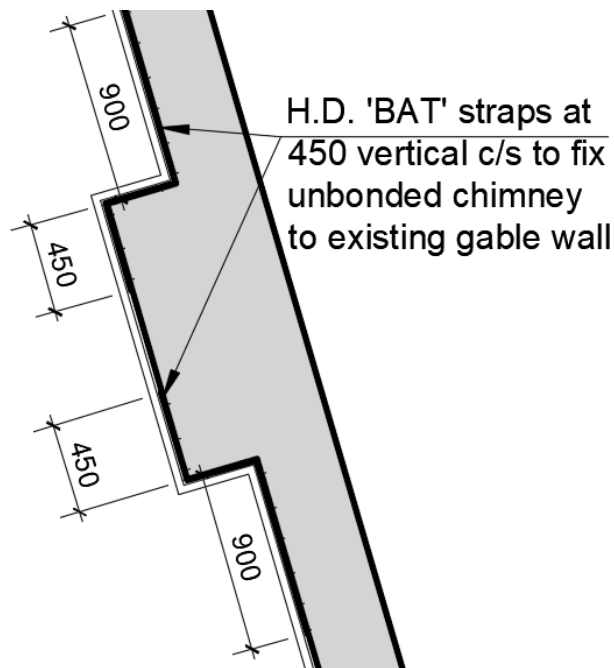

- Existing rafters at unit 5 are in poor condition. Refer to photograph 3. Therefore new 150 x 50 rafters at 400 centres are to be installed between the existing rafters. Most likely, this will be the case for the other units 4 to 1, to be confirmed on site.

Photographs on next pages.

Site Visit Report

Project Name: Brooklyn Mews
Date: 60163



Photograph 1



Photograph 2

Site Visit Report

Project Name: Brooklyn Mews

Date: 60163



Photograph 3
